



SCHEDULE - SOUTHWEST WASHINGTON REGIONAL AIRPORT - AIRPORT MASTER PLAN

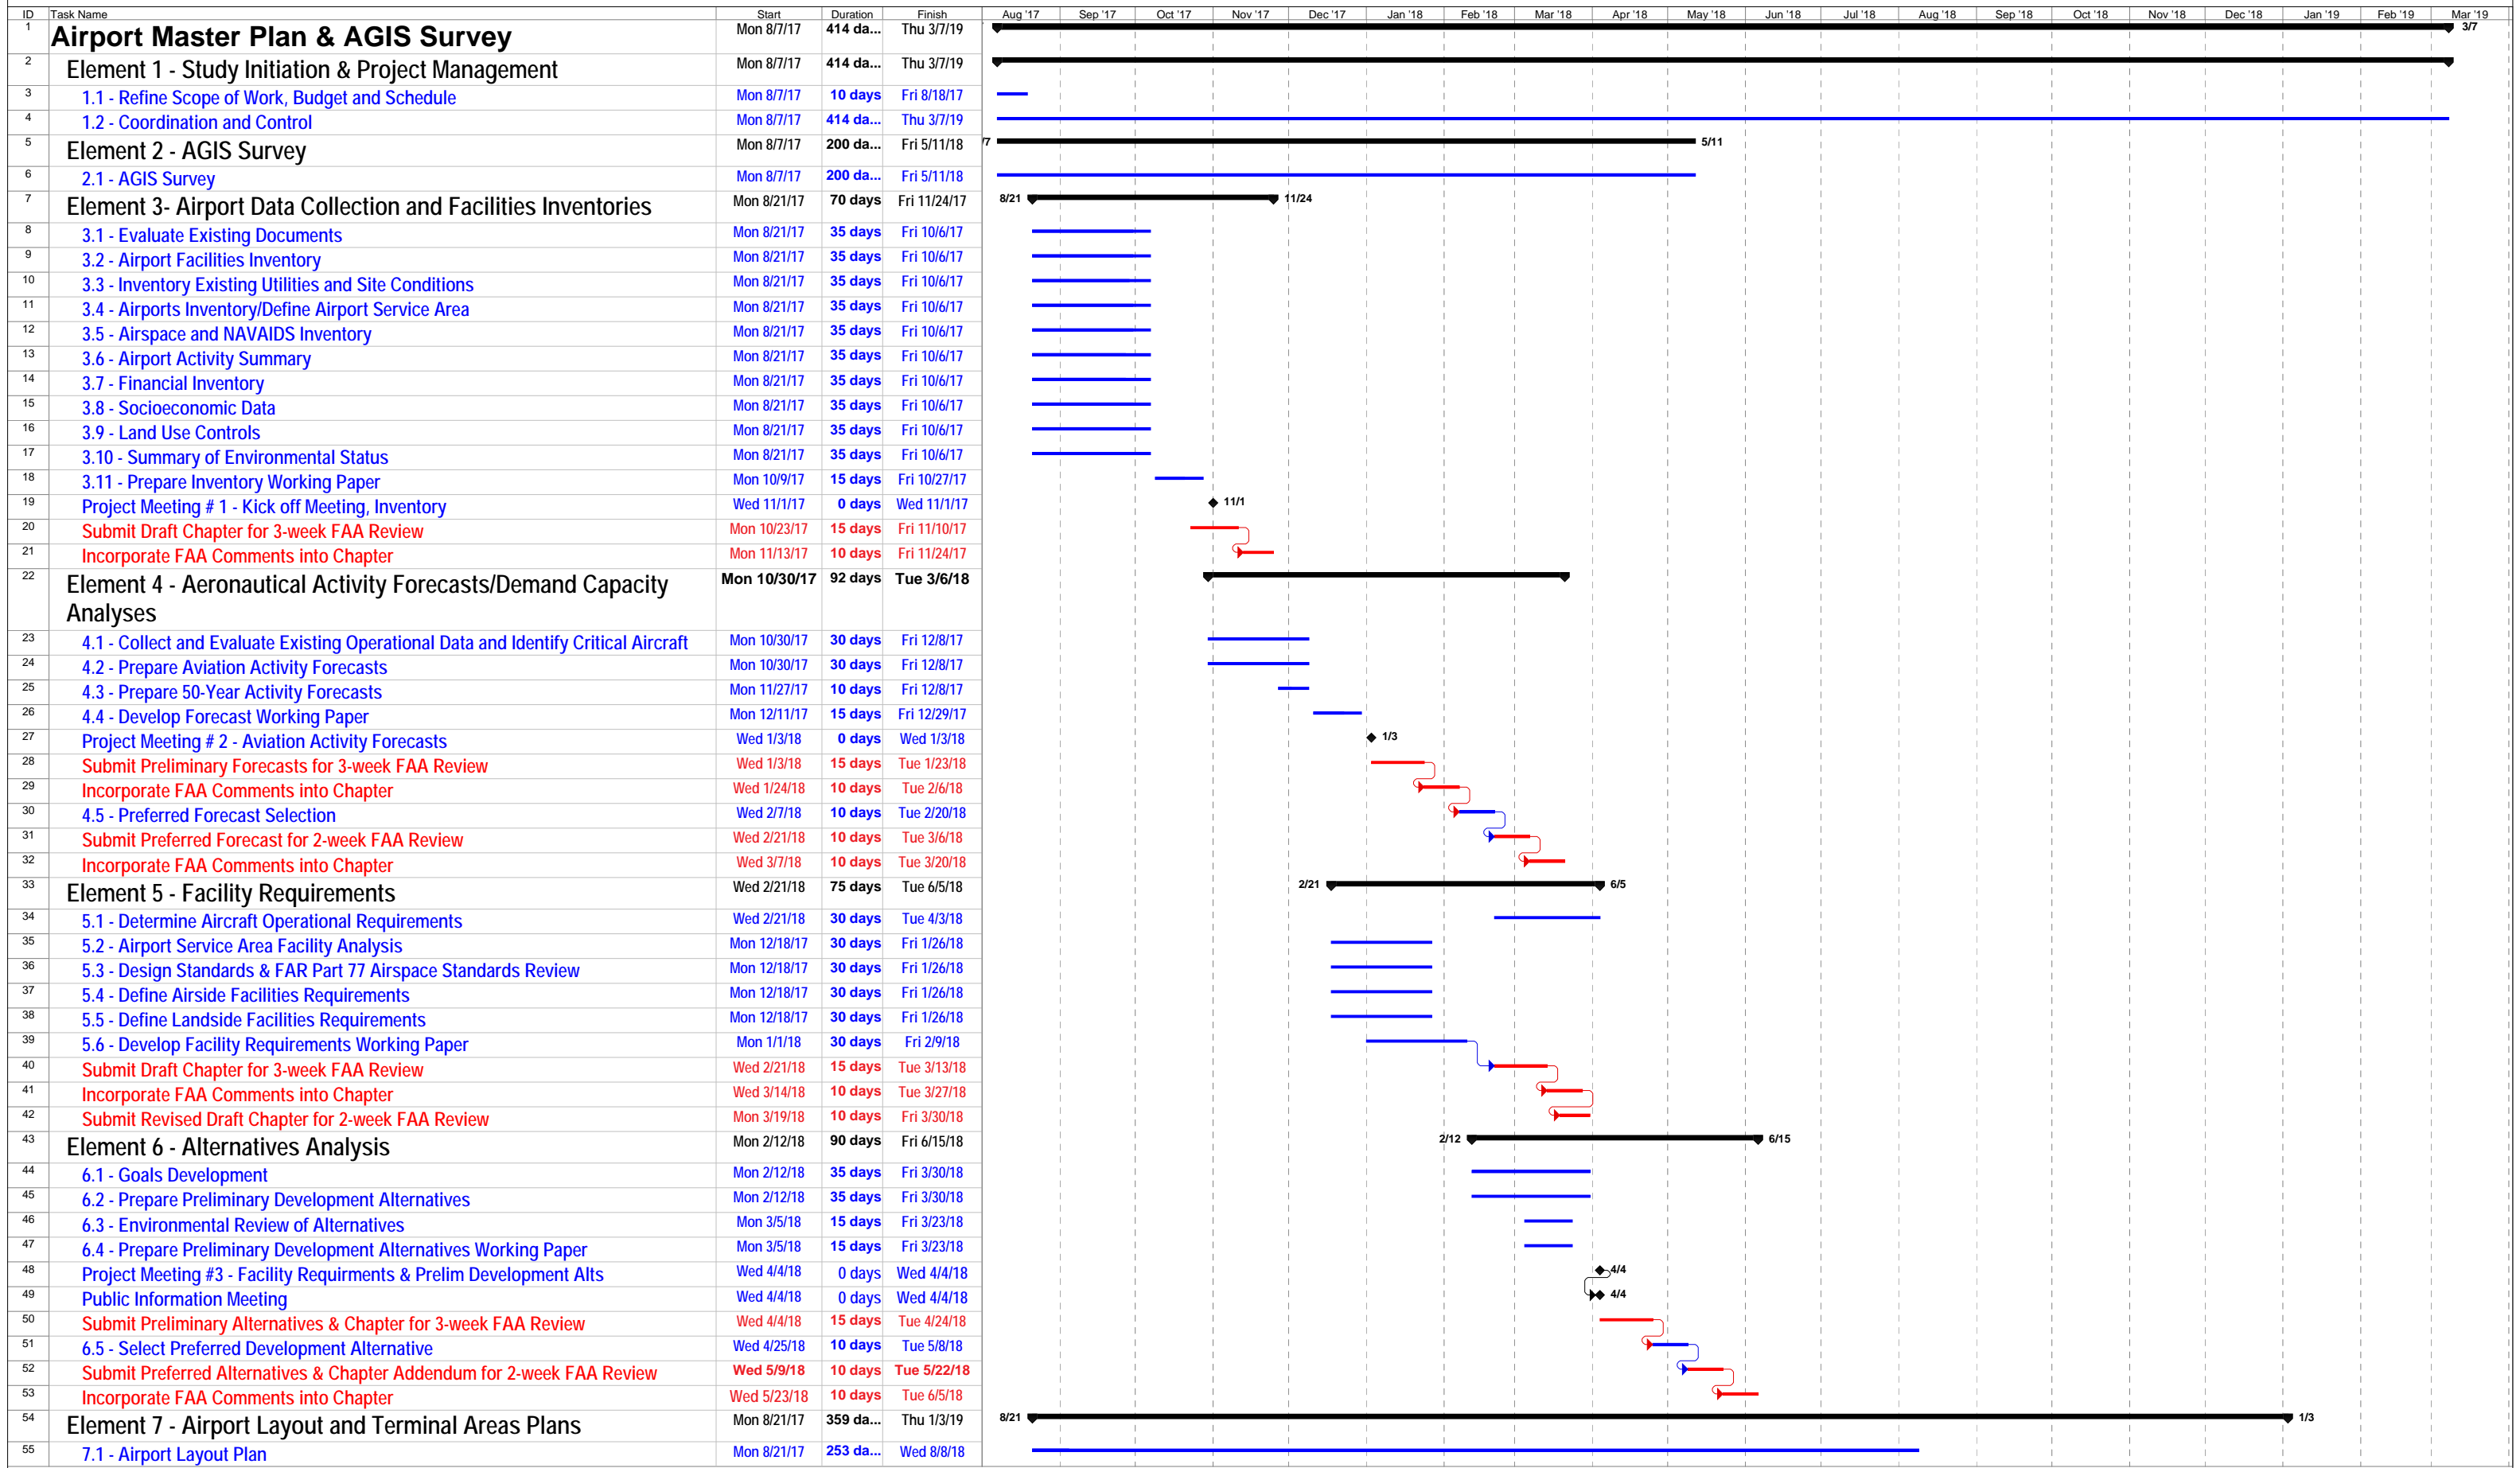

August 2017



SCHEDULE - SOUTHWEST WASHINGTON REGIONAL AIRPORT - AIRPORT MASTER PLAN

| ID | Task Name | Start | Duration | Finish | Aug '17 | Sep '17 | Oct '17 | Nov '17 | Dec '17 | Jan '18 | Feb '18 | Mar '18 | Apr '18 | May '18 | Jun '18 | Jul '18 | Aug '18 | Sep '18 | Oct '18 | Nov '18 | Dec '18 | Jan '19 | Feb '19 | Mar '19 | | | |
|-----|---|--------------|-----------|--------------|-------------------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|--|--|--|
| 56 | 7.2 - On-Airport Individual Area Plans (Shown on ALP) | Mon 8/21/17 | 253 da... | Wed 8/8/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 57 | 7.3 - Airport Airspace Drawing (FAR Part 77) | Mon 8/21/17 | 253 da... | Wed 8/8/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 58 | 7.4 - Runway Protection Zone (RPZ)/Inner Approach Plan and Profile Drawings | Mon 8/21/17 | 253 da... | Wed 8/8/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 59 | 7.5 - Approach Plan and Profile for Each Runway End | Mon 8/21/17 | 253 da... | Wed 8/8/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 60 | 7.6 - Threshold Siting Surface Drawing for Each Runway End | Mon 8/21/17 | 253 da... | Wed 8/8/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 61 | 7.7 - On-Airport Land Use Plan | Mon 8/21/17 | 253 da... | Wed 8/8/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 62 | 7.8 - Off-Airport Land Use Plan | Mon 8/21/17 | 253 da... | Wed 8/8/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 63 | 7.9 - Exhibit "A" Airport Property Map | Mon 8/21/17 | 253 da... | Wed 8/8/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 64 | Submit Preliminary ALP for 30-day FAA Review | Thu 8/9/18 | 20 days | Wed 9/5/18 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 65 | Incorporate FAA Comments into ALP | Thu 9/6/18 | 10 days | Wed 9/19/18 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 66 | Submit Draft Final ALP for 90-day FAA Review | Thu 9/20/18 | 60 days | Wed 12/12/18 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 67 | Incorporate FAA Comments into Final ALP | Thu 12/13/18 | 15 days | Wed 1/2/19 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 68 | Submit Final ALP to FAA | Thu 1/3/19 | 0 days | Thu 1/3/19 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 69 | Element 8 - Compatible Land Use Planning | Thu 5/24/18 | 70 days | Wed 8/29/18 | [Summary bar] | | | | | | | | | | | | | | | | | | | | | | |
| 70 | 8.1 - Evaluate Land Uses in Vicinity of Airport | Thu 5/24/18 | 30 days | Wed 7/4/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 71 | 8.2 - Develop Land Use Working Paper | Thu 7/5/18 | 15 days | Wed 7/25/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 72 | Submit Draft Chapter for 3-week FAA Review | Thu 7/26/18 | 15 days | Wed 8/15/18 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 73 | Incorporate FAA Comments into Chapter | Thu 8/16/18 | 10 days | Wed 8/29/18 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 74 | Element 9 - Capital Improvement Program & Cost Estimates | Thu 7/26/18 | 70 days | Wed 10/31/18 | [Summary bar] | | | | | | | | | | | | | | | | | | | | | | |
| 75 | 9.1 - Capital Improvement Program | Thu 7/26/18 | 30 days | Wed 9/5/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 76 | 9.2 - Capital Improvement Program Working Paper | Thu 9/6/18 | 15 days | Wed 9/26/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 77 | Submit Draft CIP for 3-week FAA Review | Thu 9/27/18 | 15 days | Wed 10/17/18 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 78 | Incorporate FAA Comments into CIP | Thu 10/18/18 | 10 days | Wed 10/31/18 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 79 | Element 10 - Airport Financial Plan | Thu 7/26/18 | 70 days | Wed 10/31/18 | [Summary bar] | | | | | | | | | | | | | | | | | | | | | | |
| 80 | 10.1 - Financial/Implementation Plan | Thu 7/26/18 | 30 days | Wed 9/5/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 81 | 10.2 - Financial Plan Working Paper | Thu 9/6/18 | 15 days | Wed 9/26/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 82 | Project Meeting # 4 - Preferred Alternative / CIP (Final Mtg) | Wed 11/7/18 | 0 days | Wed 11/7/18 | [Meeting diamond] | | | | | | | | | | | | | | | | | | | | | | |
| 83 | Public Information Meeting | Wed 11/7/18 | 0 days | Wed 11/7/18 | [Meeting diamond] | | | | | | | | | | | | | | | | | | | | | | |
| 84 | Submit Draft Chapter for 3-week FAA Review | Thu 9/27/18 | 15 days | Wed 10/17/18 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 85 | Incorporate FAA Comments into Chapter | Thu 10/18/18 | 10 days | Wed 10/31/18 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 86 | Element 11 - Agency Coordination | Mon 8/7/17 | 414 da... | Thu 3/7/19 | [Summary bar] | | | | | | | | | | | | | | | | | | | | | | |
| 87 | Element 12- Public Participation and Information Process | Mon 8/7/17 | 414 da... | Thu 3/7/19 | [Summary bar] | | | | | | | | | | | | | | | | | | | | | | |
| 88 | 12.1 - Identify Project Stakeholders | Mon 8/7/17 | 17 days | Tue 8/29/17 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 89 | 12.2 - Public Information Program | Mon 8/7/17 | 414 da... | Thu 3/7/19 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 90 | 12.2.1 - Project Stakeholder List | Mon 8/7/17 | 17 days | Tue 8/29/17 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 91 | 12.2.2 - Public Meeting Notices/Press Releases | Mon 8/7/17 | 414 da... | Thu 3/7/19 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 92 | 12.2.3 - Website Content for Public Website | Mon 8/7/17 | 414 da... | Thu 3/7/19 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 93 | 12.2.4 - Public Meeting Notes and Comment List | Mon 8/7/17 | 414 da... | Thu 3/7/19 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 94 | Element 13 - Recycling/Solid Waste Plan | Thu 5/24/18 | 70 days | Wed 8/29/18 | [Summary bar] | | | | | | | | | | | | | | | | | | | | | | |
| 95 | 13.1 - Waste Audit | Thu 5/24/18 | 30 days | Wed 7/4/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 96 | 13.2 - Recycling Feasibility | Thu 5/24/18 | 30 days | Wed 7/4/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 97 | 13.3 - Plan to Minimize Solid Waste Generation | Thu 5/24/18 | 30 days | Wed 7/4/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 98 | 13.4 - Operational and Maintenance Requirements | Thu 5/24/18 | 30 days | Wed 7/4/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 99 | 13.5 - Review Waste Management Contracts | Thu 5/24/18 | 30 days | Wed 7/4/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 100 | 13.6 - Potential Cost Savings or Revenue Generation | Thu 5/24/18 | 30 days | Wed 7/4/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 101 | Prepare Working Paper | Thu 7/5/18 | 15 days | Wed 7/25/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 102 | Submit Draft Chapter for 3-week FAA Review | Thu 7/26/18 | 15 days | Wed 8/15/18 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 103 | Incorporate FAA Comments into Chapter | Thu 8/16/18 | 10 days | Wed 8/29/18 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 104 | Element 14 Reports and Documentation | Mon 8/7/17 | 414 da... | Thu 3/7/19 | [Summary bar] | | | | | | | | | | | | | | | | | | | | | | |
| 105 | FAA Draft Final Report Review | Mon 9/10/18 | 129 da... | Thu 3/7/19 | [Summary bar] | | | | | | | | | | | | | | | | | | | | | | |
| 106 | Prepare Draft Final Report | Thu 11/1/18 | 15 days | Wed 11/21/18 | [Task bar] | | | | | | | | | | | | | | | | | | | | | | |
| 107 | Submit Draft Final Report for FAA 90-Day Review | Thu 11/22/18 | 60 days | Wed 2/13/19 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 108 | Incorporate FAA Comments into Final Report | Thu 2/14/19 | 15 days | Wed 3/6/19 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
| 109 | Submit Final Report to FAA for Approval | Thu 3/7/19 | 0 days | Thu 3/7/19 | [Deliverable bar] | | | | | | | | | | | | | | | | | | | | | | |
