


# SCHEDULE - HERMISTON MUNICIPAL AIRPORT - AIRPORT MASTER PLAN

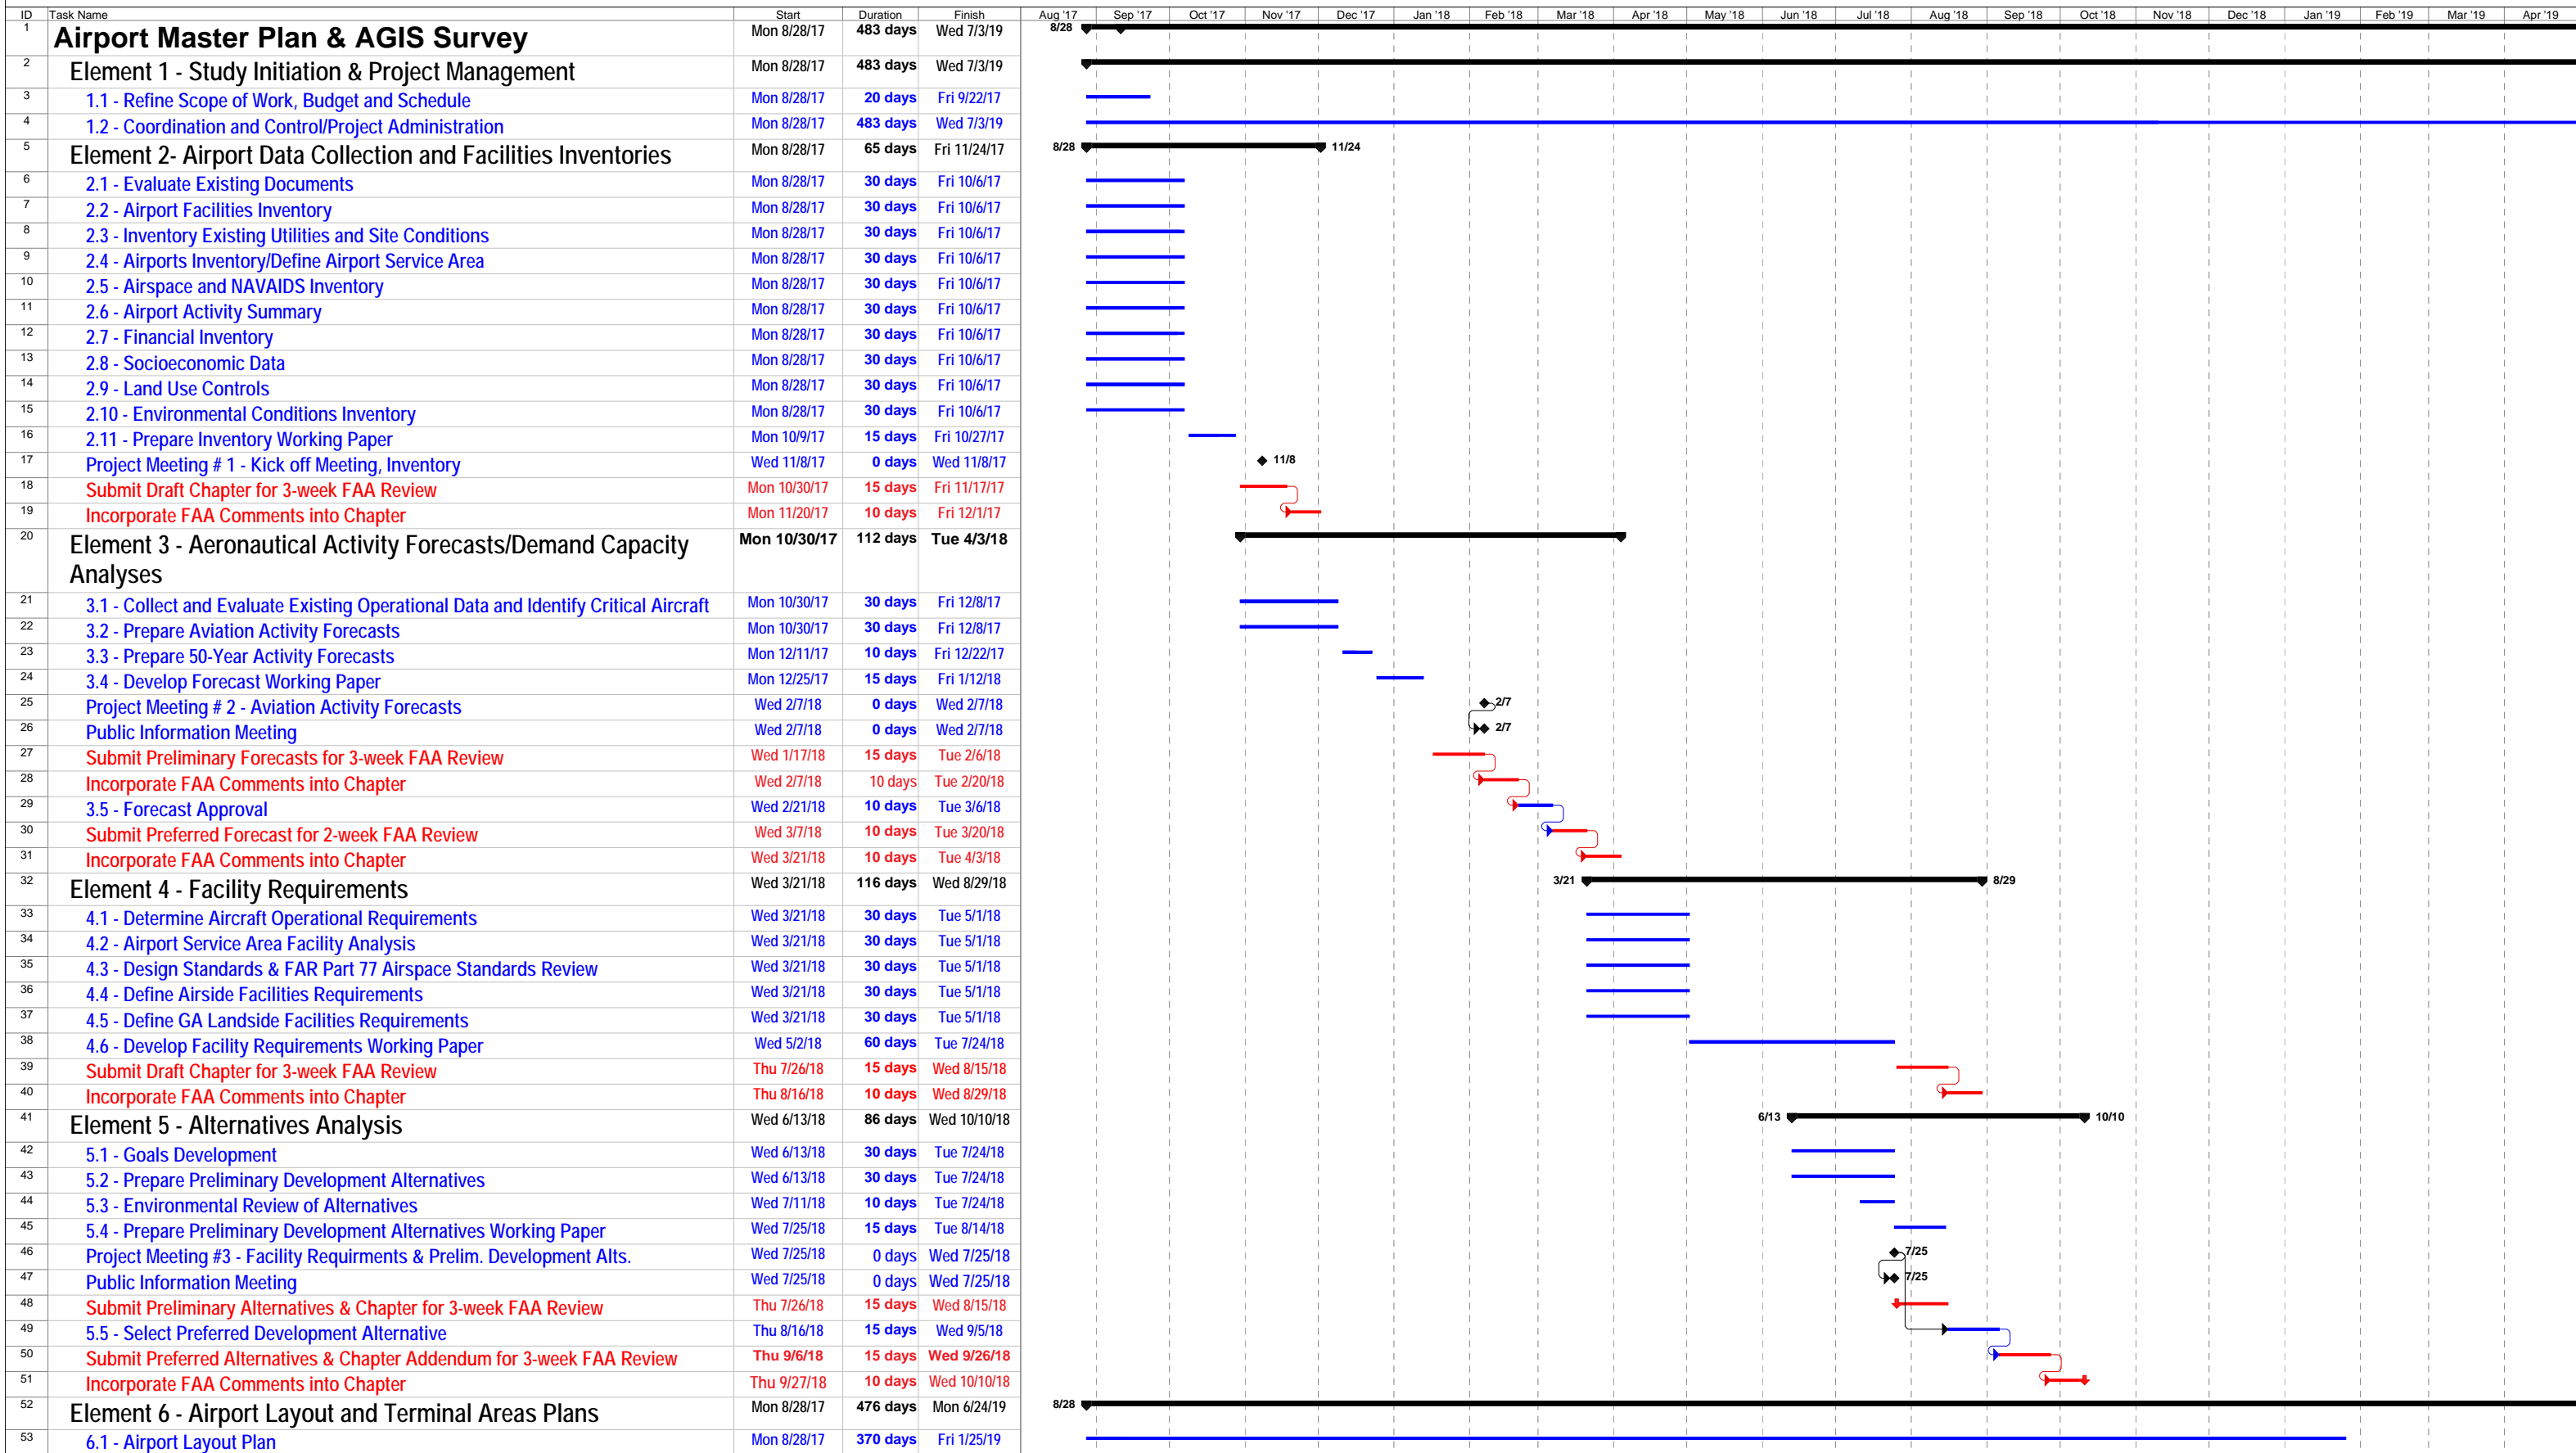

Updated June 2018

Task — Meeting ◆ Work Element Summary ▬ Review — Deliverable Deadline ↓

# SCHEDULE - HERMISTON MUNICIPAL AIRPORT - AIRPORT MASTER PLAN

ID	Task Name	Start	Duration	Finish	Aug '17	Sep '17	Oct '17	Nov '17	Dec '17	Jan '18	Feb '18	Mar '18	Apr '18	May '18	Jun '18	Jul '18	Aug '18	Sep '18	Oct '18	Nov '18	Dec '18	Jan '19	Feb '19	Mar '19	Apr '19			
54	6.2 - On-Airport Individual Area Plans (Shown on ALP)	Mon 8/28/17	370 days	Fri 1/25/19	[Task bar]																							
55	6.3 - Airport Airspace Drawing (FAR Part 77)	Mon 8/28/17	370 days	Fri 1/25/19	[Task bar]																							
56	6.4 - Runway Protection Zone (RPZ)/Inner Approach Plan and Profile Drawings	Mon 8/28/17	370 days	Fri 1/25/19	[Task bar]																							
57	6.5 - Approach Plan and Profile for Each Runway End	Mon 8/28/17	370 days	Fri 1/25/19	[Task bar]																							
58	6.6 - Threshold Siting Surface Drawing for Each Runway End	Mon 8/28/17	370 days	Fri 1/25/19	[Task bar]																							
59	6.7 - On-Airport Land Use Plan	Mon 8/28/17	370 days	Fri 1/25/19	[Task bar]																							
60	6.8 - Off-Airport Land Use Plan	Mon 8/28/17	370 days	Fri 1/25/19	[Task bar]																							
61	6.9 - Exhibit "A" Airport Property Map	Mon 8/28/17	370 days	Fri 1/25/19	[Task bar]																							
62	Submit Draft Final ALP for 30 day FAA Review	Mon 1/28/19	20 days	Fri 2/22/19	[Task bar]																							
63	Incorporate FAA Comments into Draft Final ALP	Mon 2/25/19	10 days	Fri 3/8/19	[Task bar]																							
64	Submit Draft Final ALP for 90 day FAA Review	Mon 3/11/19	60 days	Fri 5/31/19	[Task bar]																							
65	Incorporate FAA Comments into Final ALP	Mon 6/3/19	15 days	Fri 6/21/19	[Task bar]																							
66	Submit Final ALP to FAA	Mon 6/24/19	0 days	Mon 6/24/19	[Task bar]																							
67	<b>Element 7 - Capital Improvement Program &amp; Cost Estimates</b>	Thu 9/13/18	70 days	Wed 12/19/18	[Summary bar]																							
68	7.1 - Capital Improvement Program	Thu 9/13/18	30 days	Wed 10/24/18	[Task bar]																							
69	7.2 - Capital Improvement Program Working Paper	Thu 10/25/18	15 days	Wed 11/14/18	[Task bar]																							
70	Submit Draft CIP for 3-week FAA Review	Thu 11/15/18	15 days	Wed 12/5/18	[Task bar]																							
71	Incorporate FAA Comments into CIP	Thu 12/6/18	10 days	Wed 12/19/18	[Task bar]																							
72	<b>Element 8 - Airport Financial Plan</b>	Thu 9/13/18	70 days	Wed 12/19/18	[Summary bar]																							
73	8.1 - Financial/Implementation Plan	Thu 9/13/18	30 days	Wed 10/24/18	[Task bar]																							
74	8.2 - Financial Plan Working Paper	Thu 10/25/18	15 days	Wed 11/14/18	[Task bar]																							
75	Submit Draft Chapter for 3-week FAA Review	Thu 11/15/18	15 days	Wed 12/5/18	[Task bar]																							
76	Incorporate FAA Comments into Chapter	Thu 12/6/18	10 days	Wed 12/19/18	[Task bar]																							
77	Project Meeting # 4 - Preferred Alternative / CIP (Final Mtg)	Wed 11/14/18	0 days	Wed 11/14/18	[Task bar]																							
78	<b>Element 9 - Compatible Land Use Planning</b>	Mon 11/19/18	70 days	Fri 2/22/19	[Summary bar]																							
79	9.1 - Evaluate Land Uses in Vicinity of Airport	Mon 11/19/18	30 days	Fri 12/28/18	[Task bar]																							
80	9.2 - Develop Land Use Working Paper	Mon 12/31/18	15 days	Fri 1/18/19	[Task bar]																							
81	Submit Draft Chapter for 3-week FAA Review	Mon 1/21/19	15 days	Fri 2/8/19	[Task bar]																							
82	Incorporate FAA Comments into Chapter	Mon 2/11/19	10 days	Fri 2/22/19	[Task bar]																							
83	<b>Element 10 - Recycling/Solid Waste Plan</b>	Mon 11/19/18	70 days	Fri 2/22/19	[Summary bar]																							
84	10.1 - Waste Audit	Mon 11/19/18	30 days	Fri 12/28/18	[Task bar]																							
85	10.2 - Recycling Feasibility	Mon 11/19/18	30 days	Fri 12/28/18	[Task bar]																							
86	10.3 - Plan to Minimize Solid Waste Generation	Mon 11/19/18	30 days	Fri 12/28/18	[Task bar]																							
87	10.4 - Operational and Maintenance Requirements	Mon 11/19/18	30 days	Fri 12/28/18	[Task bar]																							
88	10.5 - Review Waste Management Contracts	Mon 11/19/18	30 days	Fri 12/28/18	[Task bar]																							
89	10.6 - Potential Cost Savings or Revenue Generation	Mon 11/19/18	30 days	Fri 12/28/18	[Task bar]																							
90	Prepare Working Paper	Mon 12/31/18	15 days	Fri 1/18/19	[Task bar]																							
91	Submit Draft Chapter for 3-week FAA Review	Mon 1/21/19	15 days	Fri 2/8/19	[Task bar]																							
92	Incorporate FAA Comments into Chapter	Mon 2/11/19	10 days	Fri 2/22/19	[Task bar]																							
93	<b>Element 11 - Agency Coordination</b>	Mon 9/11/17	466 days	Mon 6/24/19	[Summary bar]																							
94	<b>Element 12- Public Participation and Information Process</b>	Mon 9/11/17	466 days	Mon 6/24/19	[Summary bar]																							
95	12.1 - Identify Project Stakeholders	Mon 9/11/17	10 days	Fri 9/22/17	[Task bar]																							
96	12.2 - Public Information Program	Mon 9/11/17	466 days	Mon 6/24/19	[Task bar]																							
97	12.2.1 - Project Stakeholder List	Mon 9/11/17	10 days	Fri 9/22/17	[Task bar]																							
98	12.2.2 - Public Meeting Notices/Press Releases	Mon 9/11/17	348 days	Wed 1/9/19	[Task bar]																							
99	12.2.3 - Website Content for Public Website	Mon 9/11/17	466 days	Mon 6/24/19	[Task bar]																							
100	13.2.4 - Public Meeting Notes and Comment List	Mon 9/11/17	466 days	Mon 6/24/19	[Task bar]																							
101	<b>Element 13 Reports and Documentation</b>	Mon 9/11/17	466 days	Mon 6/24/19	[Summary bar]																							
102	Prepare Draft Final Report	Mon 2/25/19	10 days	Fri 3/8/19	[Task bar]																							
103	<b>FAA Draft Final Report Review</b>	Mon 3/11/19	76 days	Mon 6/24/19	[Task bar]																							
104	Submit Draft Final Report for FAA 90-Day Review	Mon 3/11/19	60 days	Fri 5/31/19	[Task bar]																							
105	Incorporate FAA Comments into Final Report	Mon 6/3/19	15 days	Fri 6/21/19	[Task bar]																							
106	Submit Final Report for FAA	Mon 6/24/19	0 days	Mon 6/24/19	[Task bar]																							

Updated June 2018

